Leo 325K Website — Phase 1 Plan v2 (Draft)

Oct 19, 2026 · @Rabindra Gauli

Summary

Phase 1 delivers a 6-page public website and a simple admin portal, so the council can keep leadership, clubs, resources and contact details current without a developer. Nothing is built until the District President signs off the designs and this plan.

What changed from v1:

- **Contact us** is now its own page (6 pages, not 5).
- **Admin portal** added to scope: 12 desktop screens and a mobile dashboard, already designed.
- **One brand**: the LY 2026–27 theme ("Leading with Purpose · Execution with Excellence") becomes the master look for both sites.
- Content inventory now covers club logos, Club PVST, District Lion PVST and Our Pride.
- New sections: personal data rules, technology and ownership, approval timeline, open decisions.

Design files: Public Website UI · Admin Portal · Header & Footer · Plan v1

Scope

Phase 1 = public website + admin portal. Data-heavy club features wait for Phase 2, because onboarding club and member data takes time.

Area	In Phase 1	Deferred to Phase 2
Public website	Home, About, Leadership, Clubs, Resources, Contact us (desktop + mobile), plus Privacy notice and a 404 page	Events calendar, activity reports, photo gallery
Admin portal	Sign in with email code, dashboard, messages, leadership, clubs + Club PVST, resources, site content, admin users	Club self-login, club registration, member database
Contact	Contact form delivered to the district inbox + admin Messages	Automated replies, ticketing


Area	In Phase 1	Deferred to Phase 2
Languages	English	Nepali version

The working order is fixed: collect content → finish UI/UX → walkthrough with the District President → written sign-off → build → staging review → launch.

The current site (leodistrict325knepal.org/leo.html) still shows 2025–26 leadership, so every name, title and photo for 2026–27 must be re-collected.

Sitemap

Six public pages one tap from Home; the admin portal stays separate

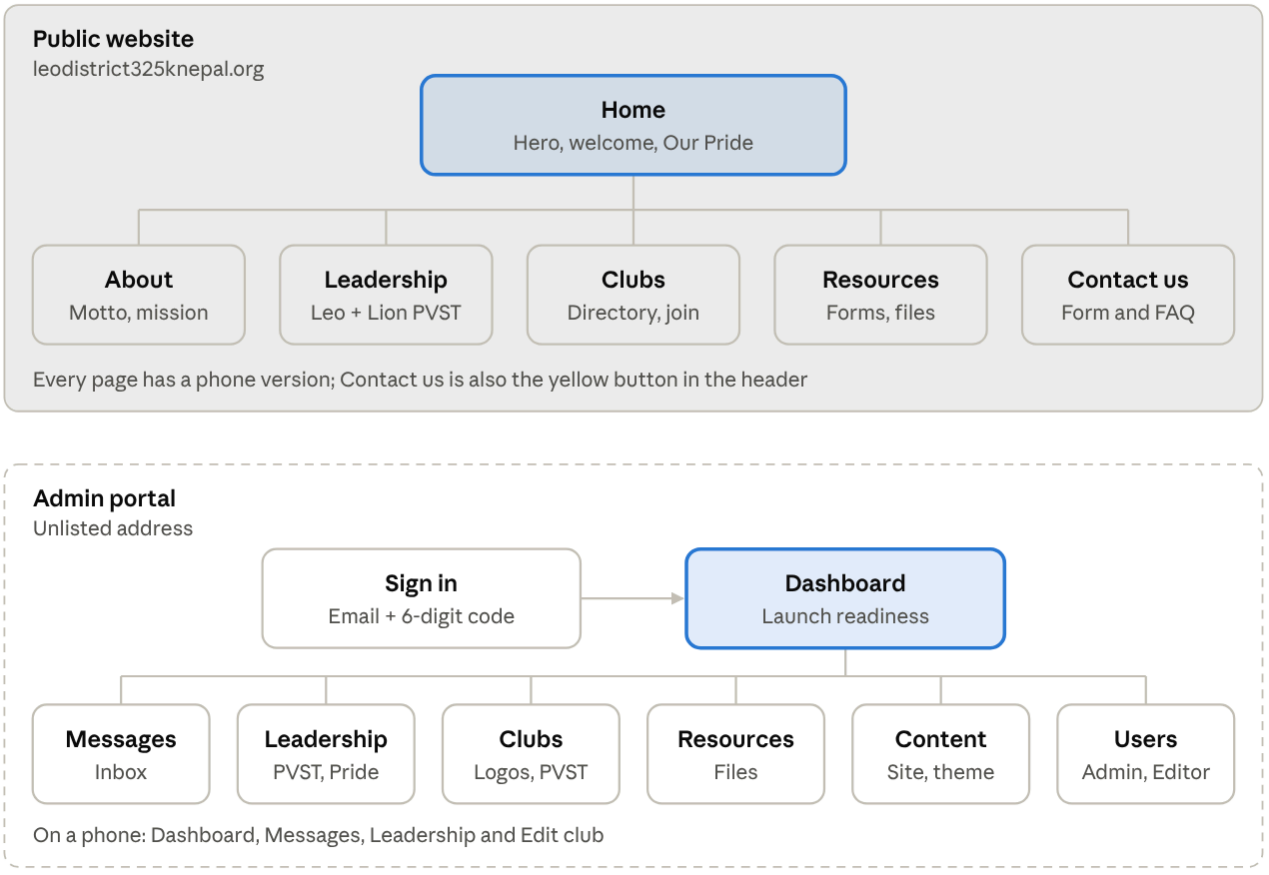

Phase 1 sitemap · 6 public pages, 8 admin screens

A flat structure keeps the main menu to five items plus the Contact button, and every page one tap from Home. Phase 2 pages slot in later without changing these URLs; the admin portal is never linked from the public site.

Brand and design system

The LY 2026–27 theme from the Header & Footer design is the master brand for every public and admin screen. The earlier navy-and-gold look and the "LEO" text placeholder are retired.

Element	Rule
Header	Desktop header, mobile header and mobile menu approved as is for Phase 1 (19 Oct 2026). Theme banner: Lions International logo, district name, LY 2026–27, Leo emblem, "Leading with Purpose / Execution with Excellence", 5 theme badges
Colours	Banner teal #244D63 → purple #762B94 · nav bar #1B3A4B · yellow #FCCC0A (buttons, active page) · orange #F6961E (divider line)
Fonts	Lato for the banner and headings, Public Sans for body text
Footer	Restyle to match the header colours; replace "DISTRICT LOGO" with the official district logo
Admin	Same banner, shorter (Admin Header), with the sidebar for navigation only
Yearly change	Banner, badges and theme words are uploaded from admin Site Content each Leo Year, so no developer is needed every July

Naming rules, used the same way on every page:

- **Leo District Council 325 K, Nepal**: full name, as on the official badge. Short form: **LDC 325 K**.
- **Leo Year 2026–27** in body text; **LY 2026–27** only in the banner. Always an en dash (–).
- **Our Pride** for the honours section (not "Hall of Honor").
- **PVST** = President, Vice President, Secretary, Treasurer.

Admin portal

The portal lets two or three district officers update the site in minutes; the District Secretary is the main content owner. Its address stays unlisted: no admin link on the public site.

Screen	What officers do there
Sign in	Official email + password, 6-digit email code on each new device
Dashboard	Launch readiness checklist, new messages, quick actions, recent activity
Messages	Read contact-form messages, mark replied, archive
Leadership	Switch Leo Year, assign District Leo PVST and District Lion PVST, publish the year's team, manage Our Pride
Add / edit person	Find an existing person first, then assign a position; photo, name, title, home club; phone and email private by default; membership ID admin only
Clubs + Edit club	Club logo, details, sponsor, charter year, Club PVST, show or hide on the directory
Resources	Upload files, set category, mark featured or coming soon
Site content	Logos, photos, yearly theme, About text, contact details, social links, contact-form test
Admin users	Invite, remove, set role

Roles (replacing the single Admin role in the current design):

Role	Who	Can
Admin	Website developer + District President (minimum 2 people)	Everything, including inviting and removing users
Editor	District Secretary, PRO	Edit and publish content, reply to messages; cannot manage users

Mobile: Phase 1 offers the dashboard plus Messages, Leadership list and Edit club on phone width. All other screens are desktop-only and say so on a phone.

Content inventory

The council provides almost all content; nothing is designed around placeholder text past the walkthrough. Update Status as items arrive.

Page	Section	Content needed	Provided by	Status
All	Brand	Official district logo (PNG + SVG), LY 2026–27 theme banner and 5 badges	Council	Not started
Home	Hero	1 hero photo of a district service event	Council	Not started
Home	Welcome	2–3 sentence welcome from the District President	Council	Not started
Home	Our Pride	Names, honour titles and photos of past leaders	Council	Not started
About	Who we are	District overview and 1–2 sentences of history	Council	Not started
About	Mission and vision	Approved wording, one or two sentences each	Council	Not started
About	Structure	Regions and how they relate to clubs	Council	Not started
About	Photo	Leos from several clubs together	Council	Not started
Leadership	District President	Name, photo, home club, message for the year, awards, Leo journey	Council	Not started
Leadership	District Leo PVST	Name, role, photo, home club for VP, Secretary, Treasurer	Council	Not started
Leadership	District Lion PVST	Governor, 1st and 2nd Vice Governors, Cabinet Secretary and Treasurer	Council	Not started
Leadership	2025–26 archive	Verify names and titles already entered (Cabinet Treasurer's home club missing)	Council	Not started

Page	Section	Content needed	Provided by	Status
Clubs	Directory	Per club: name, region, city, Alpha/Omega, charter year, sponsoring Lions club, email	Council	Not started
Clubs	Club logos	One logo per club	Each club	Not started
Clubs	Club PVST	President, VP, Secretary, Treasurer per club, with photos	Each club	Not started
Clubs	Join or start a club	Steps and who to contact	Council	Not started
Resources	Documents	Constitution, by-laws, policy, code of conduct (PDF)	Council	Not started
Resources	Forms and templates	Charter application, member registration, monthly report, officer report	Council	Not started
Resources	Brand pack	Leo logo pack and colour guidance	Council	Not started
Contact	Office details	Address, Google Maps link, office hours, promised reply time	Council	Not started
Contact	Desk emails	General, President, Secretary, Membership	Council	Not started
All	Social links	Facebook, Instagram, YouTube URLs	Council	Not started
All	SEO and footer	Page titles, meta descriptions, footer text, copyright line	Rabindra	Not started

The District Secretary collects everything into one shared folder and is the single contact for questions.

Asset specs to send the council

One spec per asset, used in this plan and in the admin portal's upload hints, so files arrive usable the first time.

Asset	Format	Minimum size	Notes
Leader and PVST portraits	JPG or PNG	800 × 800 px	Square, plain background, shoulders up, same style for all
Hero and page photos	JPG	1920 × 1080 px	Landscape, real district activity, consent of people shown
District and theme logos	SVG, or PNG with transparent background	1000 px wide	Official files only, no screenshots
Club logos	SVG, or PNG with transparent background	500 × 500 px	Square
Documents	PDF (forms also DOCX)	—	Final versions, file name = document title
Text content	Google Doc or Word	—	One file per page, names spelled exactly as they should appear

Ask for one shared folder with a subfolder per page, not photos over WhatsApp, which compresses them.

Personal data and privacy

The portal stores officers' phone numbers, emails and membership IDs (blood group is not collected in Phase 1), so every private field stays hidden unless the person agrees to show it. This follows the spirit of Nepal's Individual Privacy Act, 2075 (2018).

Data	Public site	Rule
Name, title, photo, home club	Shown	Confirmed by the person before publishing
Phone, personal email	Hidden by default	Shown only with the person's written OK; use desk emails instead
Membership ID	Never shown	Admin only
Contact-form messages	Never shown	Admins only; delete after 12 months

- Consent tickbox on the Contact form, linked to a Privacy notice page (designed).

- Photos of people at events published only with their consent (see asset specs).
- When an officer leaves, an admin removes their private details; the public archive keeps name, title and photo only.

Technology, hosting and ownership


Recommendation: build the designs as a custom site on a managed backend, because the admin portal is designed around the council's own workflow (PVST, Leo Years, Our Pride), which off-the-shelf CMS screens do not match.

Option	Fit for these designs	Running cost	Risk
A. Custom site + managed backend (recommended) e.g. Next.js + Supabase (login with email code, database, file storage)	Builds the admin portal exactly as designed	Free tiers likely cover district traffic; domain renewal only	Needs one developer to maintain code
B. WordPress + custom theme	Public site yes; admin becomes WordPress screens, not our design	Paid hosting every year	Plugin updates and security patches every month
C. Site builder (Wix, Google Sites)	Look only approximate; no Leo Year or PVST logic	Monthly plan	Locked into the platform

Ownership rules, whatever the option:

- The domain **leodistrict325knepal.org** is registered to the council (an official email), not to one person. Confirm who holds it today.
- Hosting, domain and backend logins live in a shared password manager owned by the council, with 2 people holding access.
- Cloudflare in front of the site for HTTPS, caching and DDoS protection.
- Contact-form email sent from an official address (e.g. info@) with SPF and DKIM set, so messages do not land in spam.
- Code kept in a repository the council owns, so a future web admin can take over.

Approval workflow and timeline

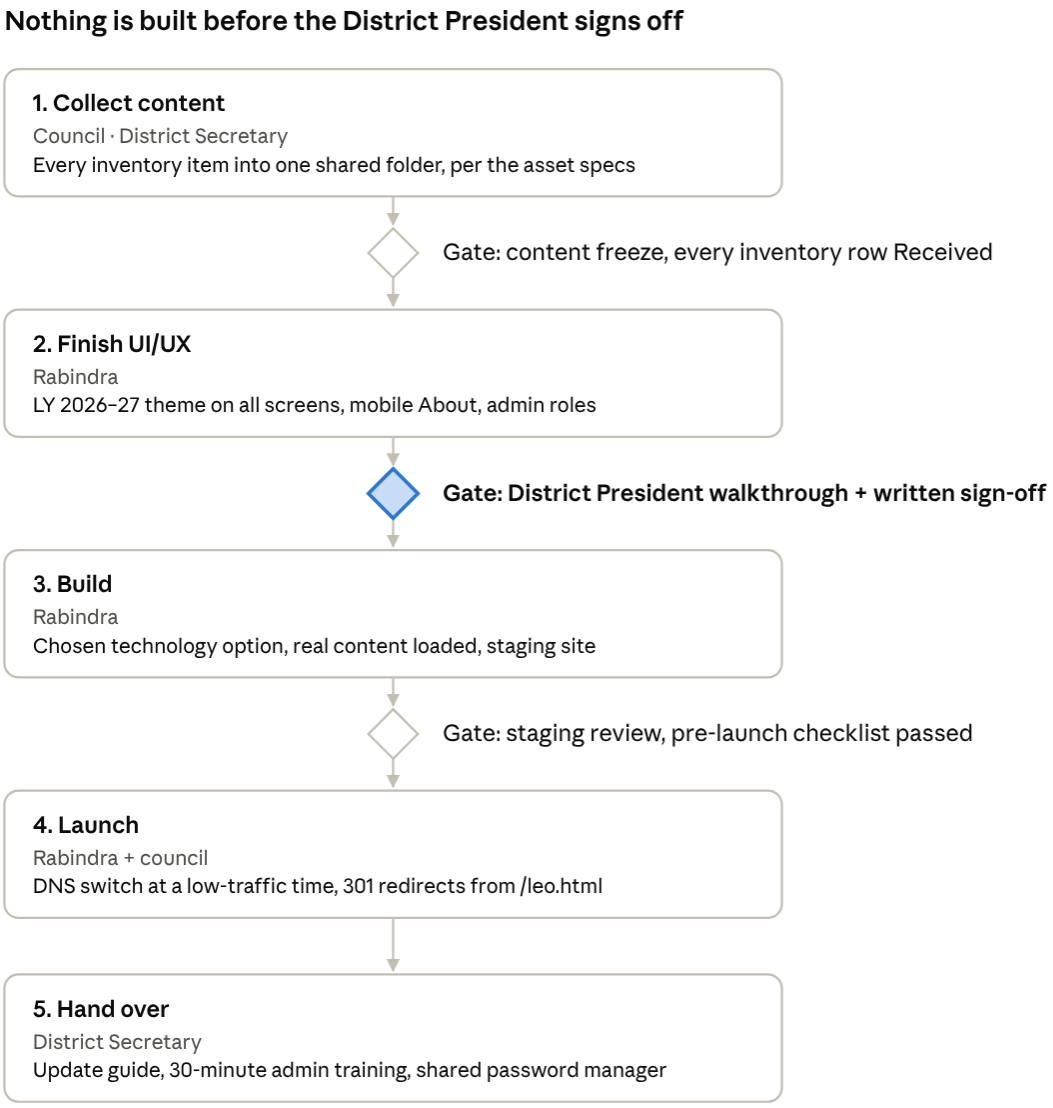

Target dates for each gate are set at the walkthrough (open decision 8).

Approval workflow · 5 stages, 3 gates

The sign-off gate is the one that cannot move: design changes after it go to a Phase 1.1 list instead of delaying the build.

Open decisions for the council

Eight decisions block the build; the first four are needed before the walkthrough.

#	Decision	Recommendation	Decides	Needed before
1	Master brand for the site	LY 2026–27 theme for all screens	District President	Walkthrough

#	Decision	Recommendation	Decides	Needed before
2	Clubs grouped by region, city or both	Region first, city as a filter	District Secretary	Walkthrough
3	Single content owner	District Secretary	District President	Walkthrough
4	Admin roles	Admin + Editor, minimum 2 Admins	District President	Walkthrough
5	Technology option (A, B or C)	Option A	District President + Rabindra	Sign-off
6	Who owns the domain and hosting accounts	Council, via official email	District President	Sign-off
7	Office address and hours to publish	Confirm; "Sunday–Friday, 10 AM–5 PM" is a placeholder	District Secretary	Content freeze
8	Target launch date	Set at the walkthrough, after content status is known	District President	Sign-off

Pre-launch checklist

Run every item on the staging site before go-live; items new in v2 are marked (new).

Content and approval

- [ ] District President has signed off the final design and content (written approval saved)
- [ ] Every leader's name, title and photo checked against the council's list
- [ ] Our Pride titles verified (e.g. "MDP 325 B", "DP 325 B") (new)
- [ ] No placeholder text, "[brackets]" or test images left
- [ ] Naming rules applied on every page: 325 K, Leo Year 2026–27, Our Pride (new)
- [ ] Spelling and grammar checked on every page

Function

- [ ] All internal and external links work (no 404s), desktop and mobile
- [ ] All PDFs open and download correctly
- [ ] Contact form test message reaches the district inbox and admin Messages (new)

- [ ] Email, phone and social links open the right target
- [ ] Custom 404 page in place

Admin portal (new)

- [ ] Sign-in email code works; at least 2 Admins set up
- [ ] An Editor can publish content but cannot manage users
- [ ] Private fields (phone, blood group, membership ID) never appear on the public site
- [ ] Admin address not linked from the public site

Mobile and browsers

- [ ] Tested on at least one real Android and one iPhone
- [ ] Tested in Chrome, Edge, Safari and Firefox
- [ ] Menu, tables and images usable at phone width, no sideways scrolling

Performance

- [ ] Images compressed (WebP or optimised JPG) and lazy-loaded; theme badges sized for mobile
- [ ] PageSpeed Insights mobile score checked and major issues fixed
- [ ] Pages usable on a slow mobile connection

Accessibility

- [ ] Every image has meaningful alt text
- [ ] One H1 per page, headings in order
- [ ] Text contrast passes, and the menu works by keyboard

SEO and sharing

- [ ] Unique title and meta description per page
- [ ] Clean URLs (/about, /leadership, /clubs, /resources, /contact)
- [ ] sitemap.xml and robots.txt published (admin paths excluded)
- [ ] Open Graph image and text so links preview well on Facebook and WhatsApp
- [ ] Favicon in place

Security

- [ ] HTTPS forced, valid certificate, no mixed content
- [ ] Security headers set: HSTS, CSP, X-Frame-Options, X-Content-Type-Options
- [ ] Contact form protected against spam (rate limit or CAPTCHA) (new)
- [ ] No test accounts or debug pages left
- [ ] Cloudflare in front for DDoS protection and caching

- [ ] Backup taken and a restore tested

Go-live

- [ ] 301 redirects from old URLs (e.g. /leo.html) to the new pages
- [ ] DNS change planned at a low-traffic time, with rollback ready
- [ ] Google Search Console verified and sitemap submitted
- [ ] Analytics installed
- [ ] Final smoke test on the live domain after the DNS switch

After launch

The site stays accurate only if updates have an owner and a schedule; the District Secretary owns it, with Rabindra as technical support.

- [ ] Hand over a one-page "how to update" guide and a 30-minute admin training to the content owner
- [ ] Record hosting, domain, renewal dates and logins in the council's shared password manager
- [ ] Weekly: answer contact-form messages within the promised reply time
- [ ] Monthly: check links, backups and software updates
- [ ] Each new Leo Year (July): upload the new theme banner and badges, publish the new district team and Club PVST, archive the previous year
- [ ] Review Phase 2 readiness: club login, club registration, events and activities, Nepali version
